

Memo

Project: National Paediatric Hospital

Report Type: Summary of Dust Monitoring Results

Period of Monitoring: 4th April 2018 – 4th May 2018

Introduction

The requirement for Dust Monitoring on site is laid out in the Project Environmental Impact Statement (EIS) that would have been submitted as part of the Planning Permission for the project. A number of monitoring points around the perimeter of the site are used to record dust levels. The location and number of dust monitors may vary throughout the project depending on activities on site.

Dust Monitoring.

The monitors are examined monthly and the levels of dust recorded are compared to a dust limit of 350mg/m²/day set out in the Project EIS. The monitoring points are monitored on a 'trigger level' basis - so if a predetermined level of dust is exceeded the Main Contractor shall review work processes and modify as required to reduce the level of dust generated.

Number of Monitors on Site during Monitoring Period:

Eleven.

Location of Monitors:

The location of dust monitoring points for April 2018 (D1, D2, etc.) can be seen in Figure 1. The previous dust monitor locations for the period April to September 2017 are shown in Figure 2 for reference.

Observations:

The dust monitoring period for March extends from 4th April 2018 to 4th May 2018. (Results for March included testing up to and including 3rd March, meaning all working days on site have been captured in the dust monitoring results)

Over this period, all monitors were tested on a monthly basis i.e. once. Monitor D8, located to the rear of O'Reilly Avenue, has been replaced and the results for April are included in this report.

Works on site during this monitoring period include, but are not limited to:

- Construction works for the Utility Tunnel at the Energy Centre.
- Excavation and pile capping near the hospital entrance and South Circular Road.
- Excavation and piling near Cameron Square.
- Road construction and pile cropping near Brookfield Clinic.
- Pile cropping and piling near Linear Park.

Overall, all dust monitors on site showed levels of dust lower than the levels specified in the Project EIS, less than 350mg/m²/day.

Memo

Dust Monitoring Point D3 recorded the highest reading and is located near the Rialto LUAS. The dust deposition rate was approximately 37% of the deposition rate limit specified in the Project EIS. During this monitoring period, there were piling works ongoing in this area which may have resulted in this higher reading, however, the monitoring result remains below the limit set out in the Project EIS.



Figure 1. Location of Dust monitors on site (January 2018).

Memo

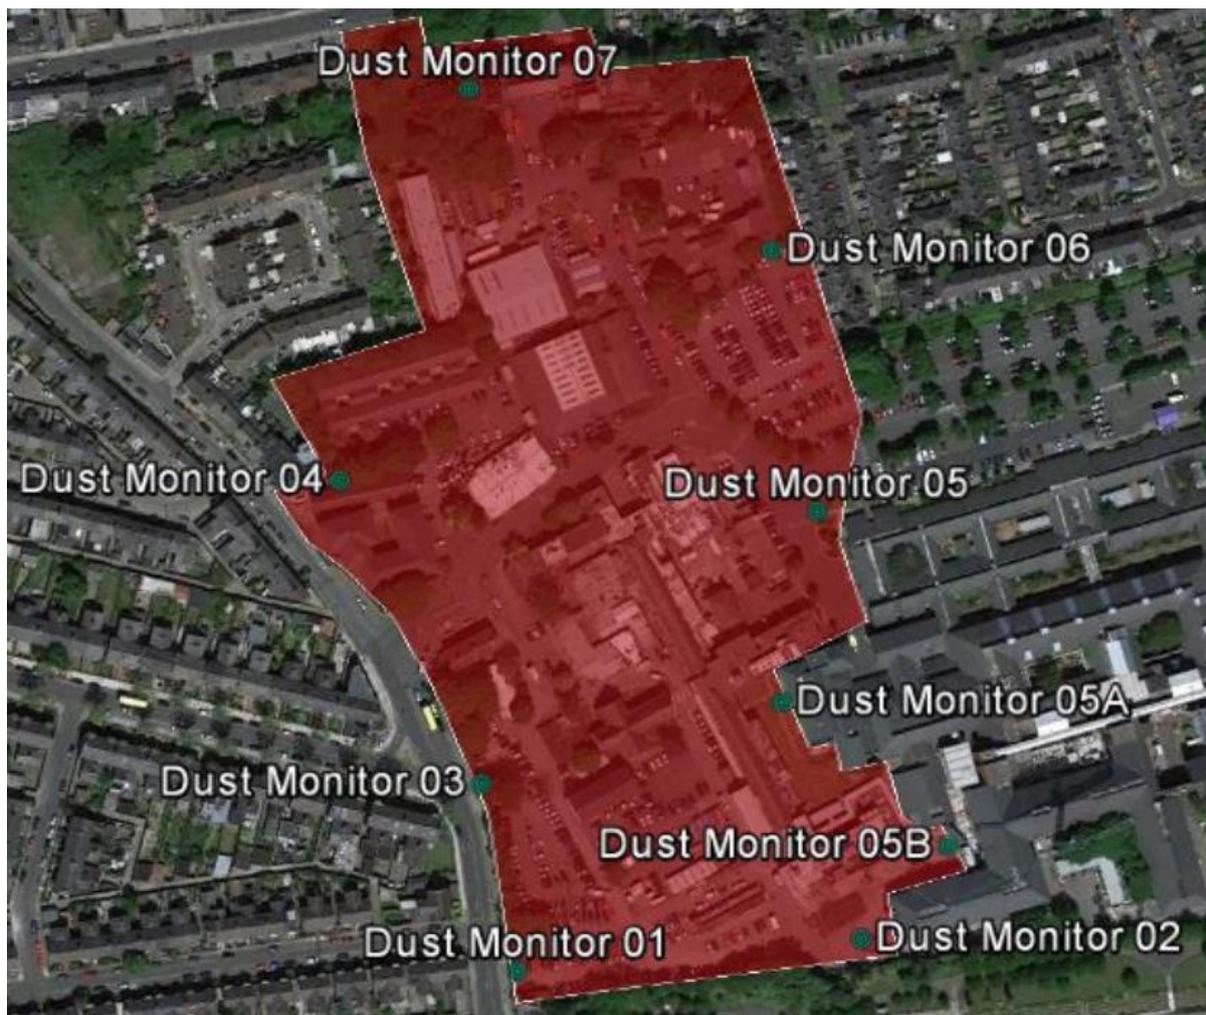


Figure 2. Previous location of Dust monitors on site (April 2017 to August 2017).
